

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	15 February 2025
Team ID	SWUID2026297489
Project Name	Auto Ticket Classification using Flow Designer
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Project Setup	USN-1	As an admin, I can create a new Local Update Set (Project Update Set) and make it current, so all my changes are tracked.	2	High	Developer
Sprint-1		USN-2	As an admin, I can document the business use case and the 6 business requirements, so the scope of the helpdesk automation is clear.	3	High	Developer
Sprint-1	Data Model	USN-3	As an admin, I can create the custom table Incident WorkFlow (u_incident_workflow) with auto-number (INC, 5 digits).	5	High	Developer
Sprint-1		USN-4	As an admin, I can add the fields Caller, Short description, Description, Assigned group and Assigned to with correct data types.	5	High	Developer
Sprint-1		USN-5	As an admin, I can add choice lists for Category, Subcategory and State using Form Design.	5	High	Developer
Sprint-2	Dependent Choices	USN-6	As an admin, I can make Subcategory dependent on Category (Configure Dictionary, Use dependent field).	5	High	Developer
Sprint-2		USN-7	As an admin, I can map each Subcategory to its Category (Wi-Fi to Network, Projector to Hardware, etc.) so only valid options show.	3	High	Developer
Sprint-2	Auto Classification Flow	USN-8	As an admin, I can create the flow Auto Classify School IT Tickets with trigger Record Created and condition Category is empty.	5	High	Developer
Sprint-2		USN-9	As a student, my ticket is classified as Network / Wi-Fi when the short description contains Wi-Fi or Network.	4	High	Developer
Sprint-2		USN-10	As a student, my ticket is classified as Hardware / Projector when the short description contains Projector.	3	High	Developer
Sprint-3		USN-11	As a student, my ticket is classified as Access / Forgot Password when the short description contains Forgot password.	3	High	Developer
Sprint-3		USN-12	As a student, my ticket is classified as Performance / Slow Computer when the short description contains Slow computer.	3	High	Developer
Sprint-3		USN-13	As an admin, I can extend the keyword conditions (WiFi, Login, Hanging) so more tickets are classified correctly.	4	Medium	Developer
Sprint-3		USN-14	As an IT agent, I can see unmatched tickets handled by a default (Else) branch, so no ticket is left unclassified.	3	Low	Developer
Sprint-3	Email Notification & Activation	USN-15	As a student, I receive a confirmation email (Send Email to Caller's email) once my ticket is created.	5	High	Developer
Sprint-3		USN-16	As an admin, I can activate the flow so it runs automatically on every new ticket.	2	High	Developer

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-4	Testing & Validation	USN-17	As a tester, I can test Scenario 1 (WiFi not working in library) and confirm Network / Wi-Fi is filled.	3	High	Developer
Sprint-4		USN-18	As a tester, I can test Scenario 2 (Projector not turning on) and confirm Hardware / Projector is filled.	3	High	Developer
Sprint-4		USN-19	As a tester, I can verify the email under System Logs, Emails and use Preview Email to see the message.	3	High	Developer
Sprint-4		USN-20	As an admin, I can run data validation and security checks (mandatory fields, no duplicate numbers, reference fields, access roles).	5	Medium	Developer
Sprint-4	Deployment & Documentation	USN-21	As an admin, I can mark the update set Complete and Export to XML so it can be moved to another instance.	3	High	Developer
Sprint-4		USN-22	As a team, we can finalize the project documentation and conclusion.	3	Medium	Developer
			Total story points (4 sprints)	80		

Project Tracker, Velocity & Burndown Chart: (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	20	6 Days	24 Oct 2022	29 Oct 2022	20	29 Oct 2022
Sprint-2	20	6 Days	31 Oct 2022	05 Nov 2022	20	05 Nov 2022
Sprint-3	20	6 Days	07 Nov 2022	12 Nov 2022	20	12 Nov 2022
Sprint-4	20	6 Days	14 Nov 2022	19 Nov 2022	20	19 Nov 2022
Total	80	24 Days			80	


Velocity:

The team has a **6-day sprint duration** and a velocity of **20 story points per sprint** (80 story points completed over 4 sprints, so the average velocity is $80 / 4 = 20$ points per sprint). The team's average velocity (AV) per iteration unit (story points per day) is:

$$AV = \text{Velocity} / \text{Sprint duration} = 20 / 6 = 3.33 \text{ story points per day}$$





Burndown Chart:

A burndown chart is a graphical representation of work left to do versus time. The grey dashed line is the ideal burndown (80 points falling evenly to 0 over 24 days). The blue line is the actual work remaining. All four sprints finished on their planned end dates, so the actual line meets the ideal line at the end of every sprint (60, 40, 20 and 0 points remaining).

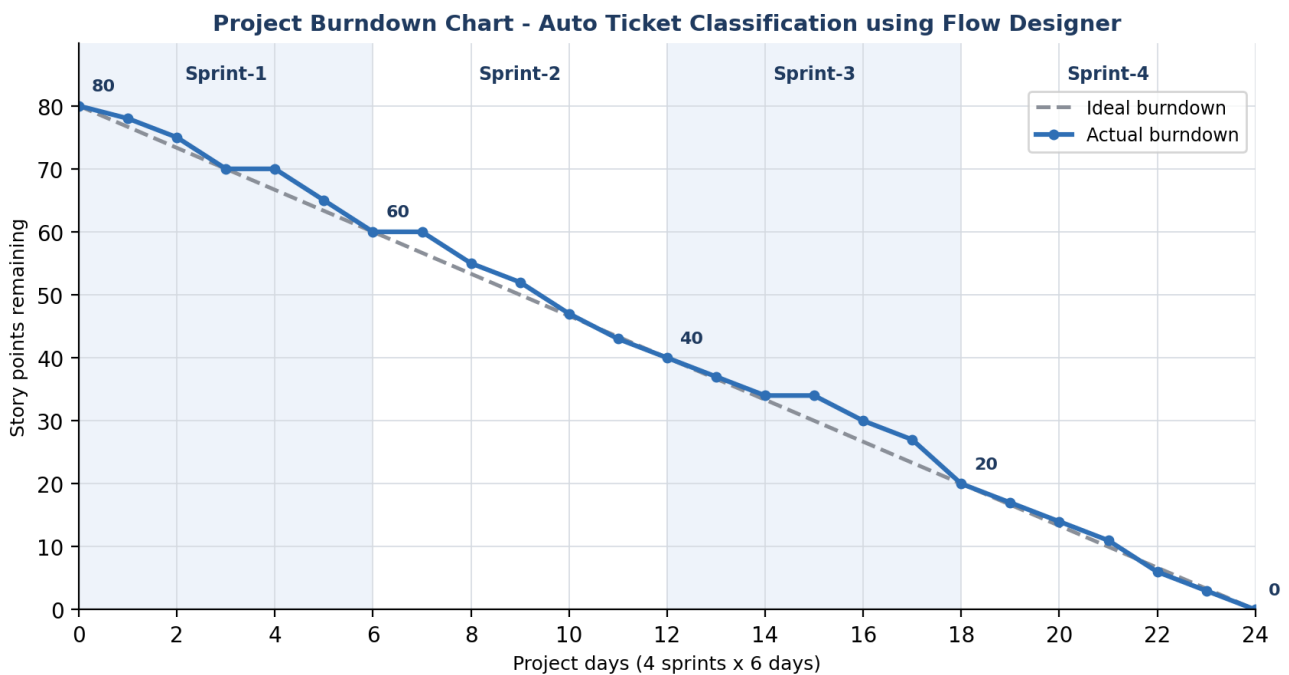

Sprint-wise Burndown Charts

Each sprint starts with 20 story points and burns down to 0 within its 6 days.

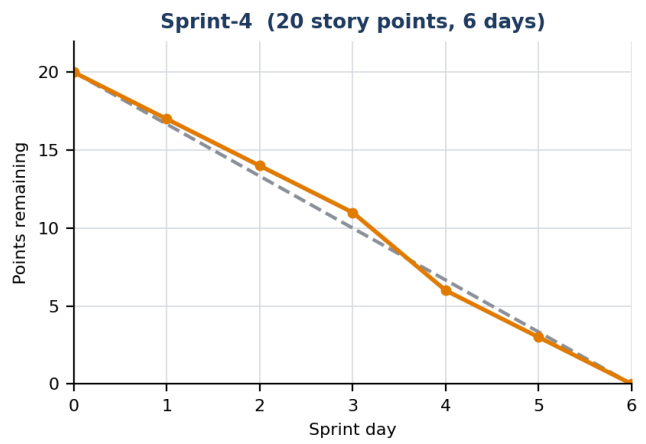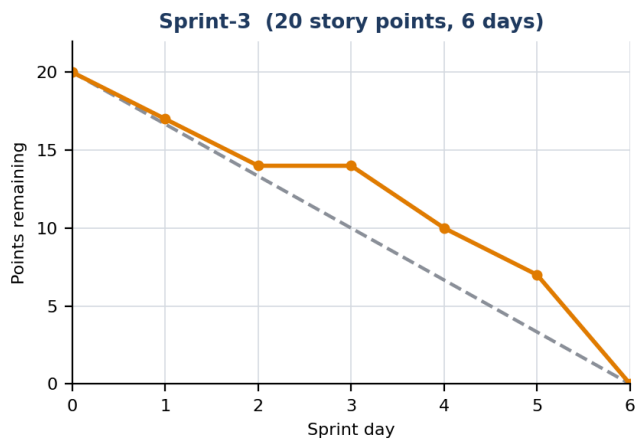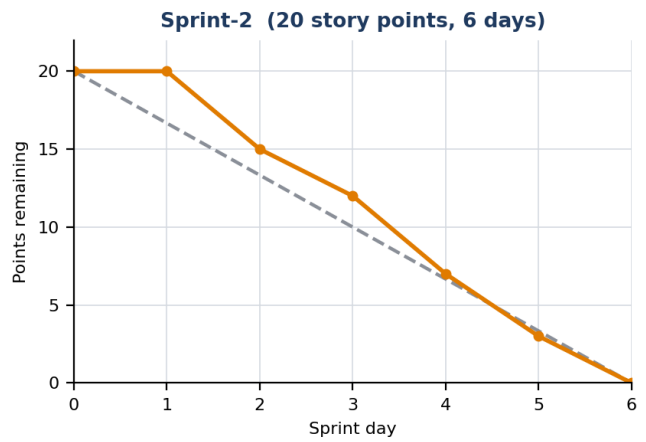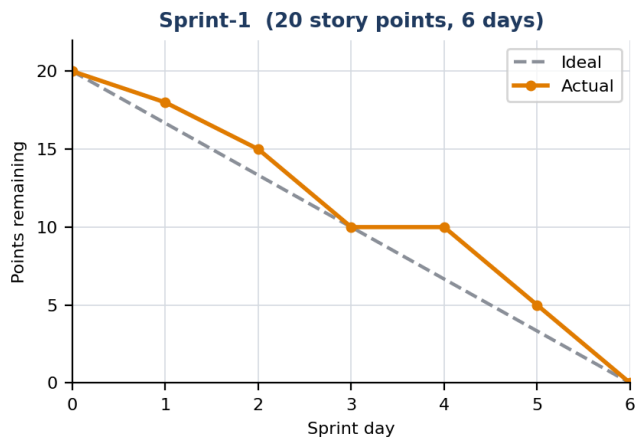

Sprint	Points at start	Points completed	Points remaining at sprint end
Sprint-1	80	20	60
Sprint-2	60	20	40
Sprint-3	40	20	20
Sprint-4	20	20	0
